



Project Update - TH 13 – 150th Street Improvements

Project Contacts

Contractor - S.M. Hentges & Sons, Inc

Project Superintendent
Steve Engstrom
612-919-4655 (cell)
952-492-5700 (office)

Project Superintendent
Kevin Oldridge
612-919-4679 (cell)

Lead Project Representative
John Wichman - City of Savage
612-490-8744 (cell)
952-882-2675 (office)

Project Engineer
Chris McKenzie – SEH
952-912-2607 (direct)

The project field office is located in the Bethesda Church parking lot.

Construction will be completed by Fall 2016.

Please drive safely through the work zone!

Future project updates will be provided online at www.sehinc.com/online/13-150.

August 4, 2016 | Project Update No. 6

Major Highway 13 Traffic Switch Coming

Trunk Highway 13

On Wednesday, August 10th, both directions of Highway 13 traffic will be shifted to the new northbound lanes, allowing the new southbound lanes to be constructed. We thank you for your patience as the contractor works to get the traffic switch accomplished.

The lanes will be narrow, so please use caution when using this new, temporary TH 13 corridor. If you have a wide vehicle, such as a wide boat trailer, please consider using alternate routes.

City of Prior Lake Local Streets

150th St, Estate and Glasgow have been graded, and vehicles can have access on the gravel base. Access to TH 13 will be **Green Oaks Trail** until mid-October. Homeowners living on **Estate, 150th and Glasgow Trail** within the project area will be contacted individually for your driveway access information for upcoming curb & gutter and blacktop paving installations in mid to late August.

The majority of **Estate, 150th and Glasgow Trail** work will likely conclude by the Labor Day weekend.

Oakland Beach Ave will not have access to TH 13 beginning Wednesday August 10. **Rustic Road** will be the only access to that neighborhood.

150th St and Oakland Beach Ave will regain access to TH 13 in mid-October.

City of Savage Local Streets

150th St and Zinran Aves on the Savage side have been paved, and beginning August 10th, will each have right turn access only, both in and out from TH 13.

Minor work that does not impact traffic will occur where the pavement has been placed. Please use caution as crews work to install the final pieces to these areas.

Please see the enclosed map for alternate routes.

Project Contacts

Contractor - S.M. Hentges & Sons, Inc
Project Superintendent
Steve Engstrom
612-919-4655 (cell)
952-494-5700 (office)

Lead Project Representative
John Wichman - City of Savage
612-490-8744 (cell)
952-882-2675 (office)

Project Engineer
Chris McKenzie – SEH
952-912-2607 (direct)

The project field office is located in the Bethesda Church parking lot.

Construction will be completed by Fall 2016.

Please drive safely through the work zone!

Future project updates will be provided online at www.sehinc.com/online/13-150.

School Buses

With school starting soon, please watch for instructions from the School District for specific bus stop and route instructions. The project team is working with the school district to ensure bus stops and routes are maintained.

Please talk with your children and help them keep a safe distance from construction activities. Safety is our top priority, especially as kids and buses begin the new school year.

The Overall Project


The project includes reconstruction of TH 13 and realignment of 150th Street. An overall layout of the project is provided below. For a more detailed view – this image and other information is available on the project website at www.sehinc.com/online/13-150.

Construction Site Safety

Please take care as you navigate through the work zone. Warn children to stay away from equipment, pipes and other materials that may be staged for installation. Be aware of heavy machinery operating in the work zone and the possibility of deep trenches or irregular ground surfaces in areas that work is occurring. The Contractor will make work areas safe each night before leaving the site.

Work zone speed limits will remain at 30 mph. Access to all homes, businesses and schools will be maintained. We ask that you avoid bicycling on TH 13 due to the reduced lane widths and frequent construction traffic.

Trucks will be entering and exiting normal traffic patterns to serve the project. Please give the trucks lots of room, and don't follow them into the construction areas. The contractor may provide flaggers to direct traffic as necessary for the safety of both the motoring public and the workers.

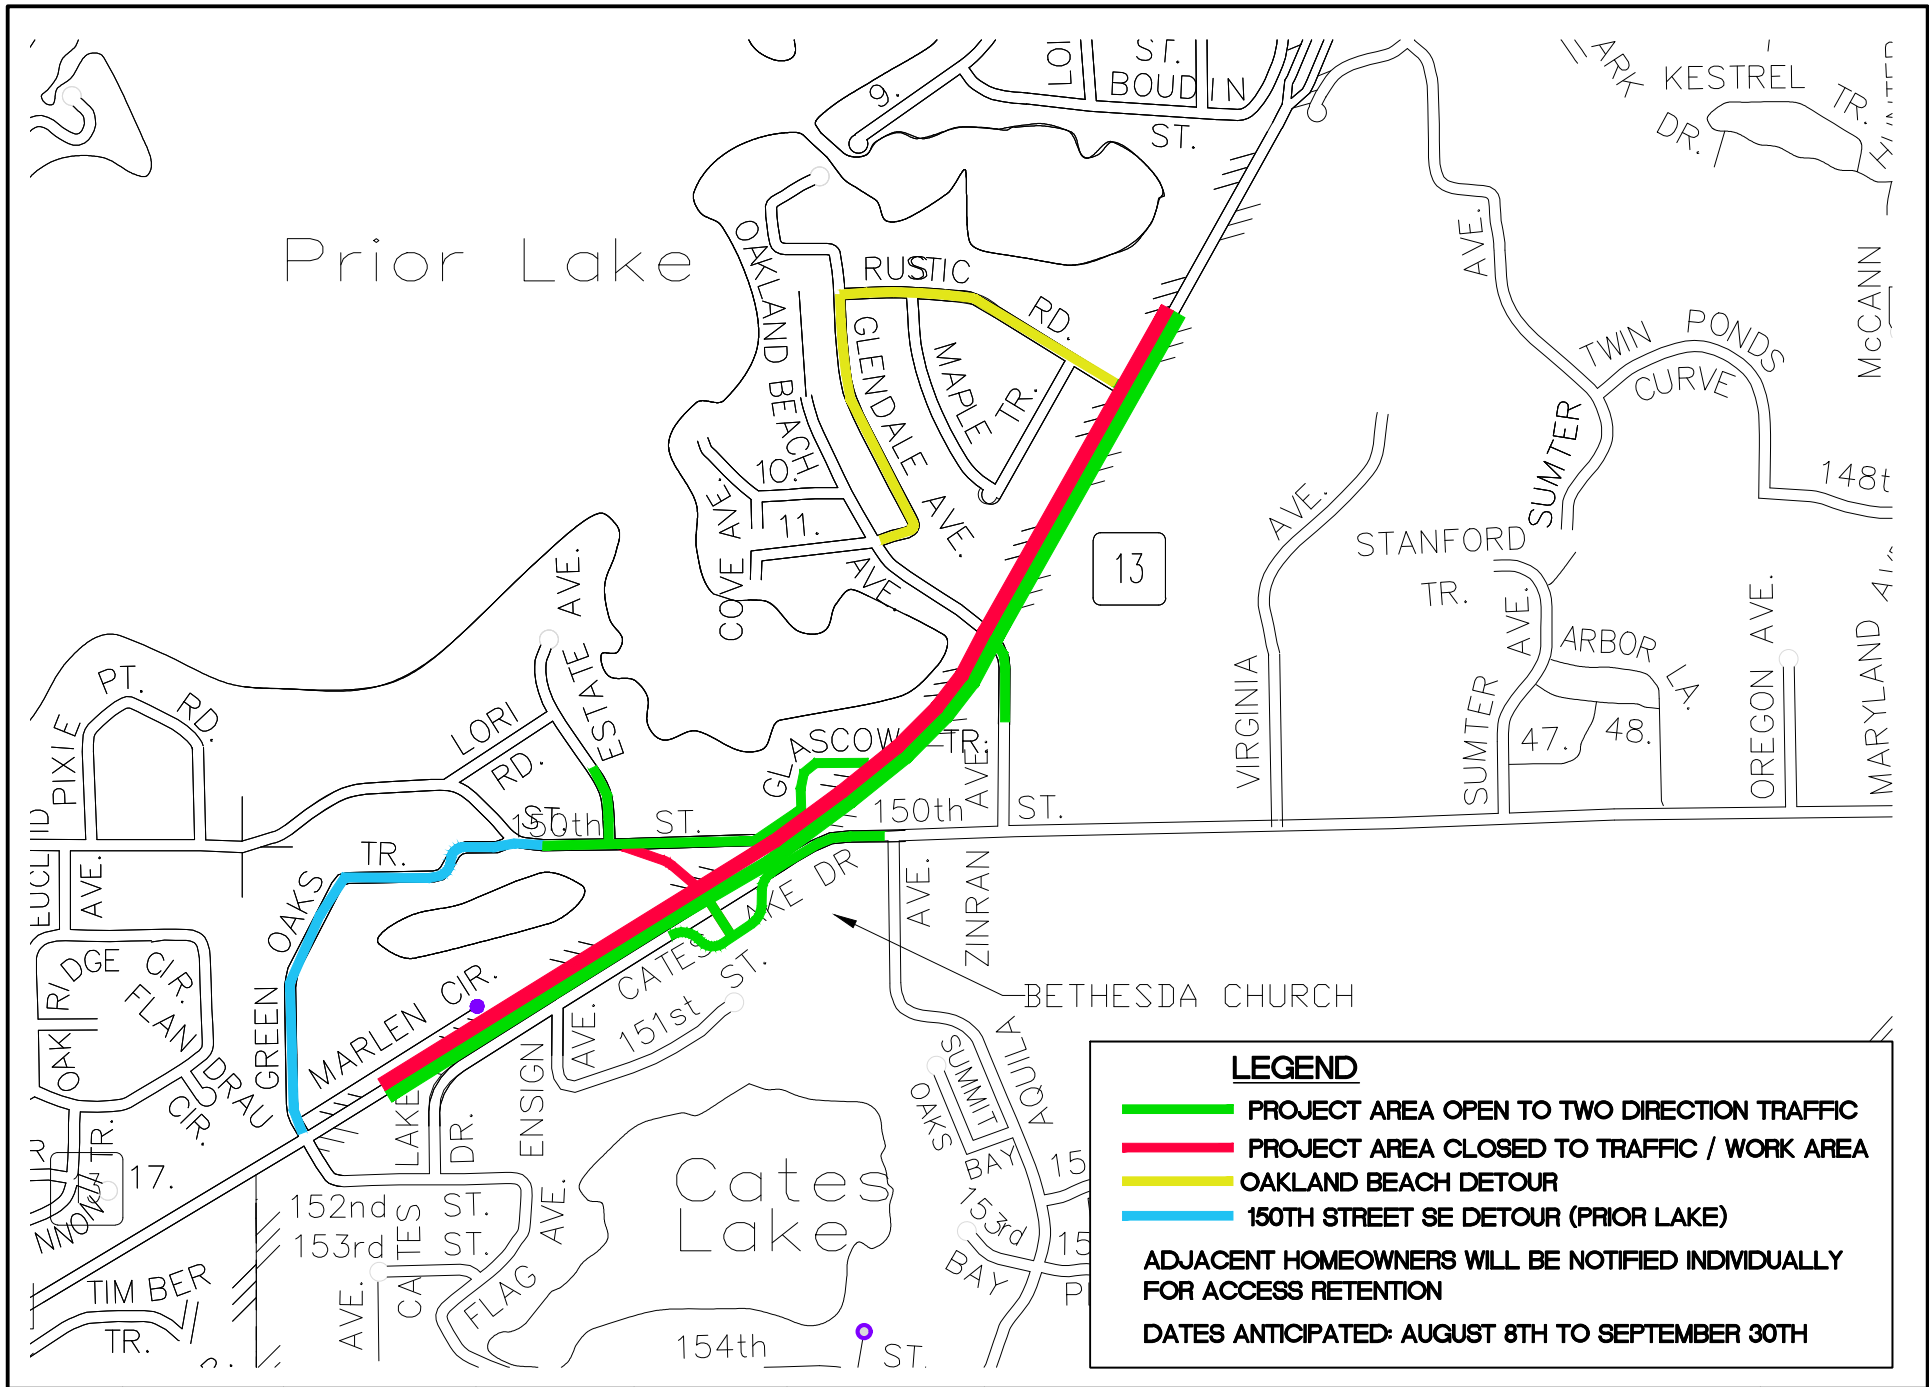

					FILE NO. SAVAG133360	Phase 3 Traffic Control Savage and Prior Lake - TH 13 / 150th Street Intersection Reconstruction	EXHIBIT NO. 3
					DATE: 7/13/16		
